UCSC McHenry Library - Short Interval Schedule
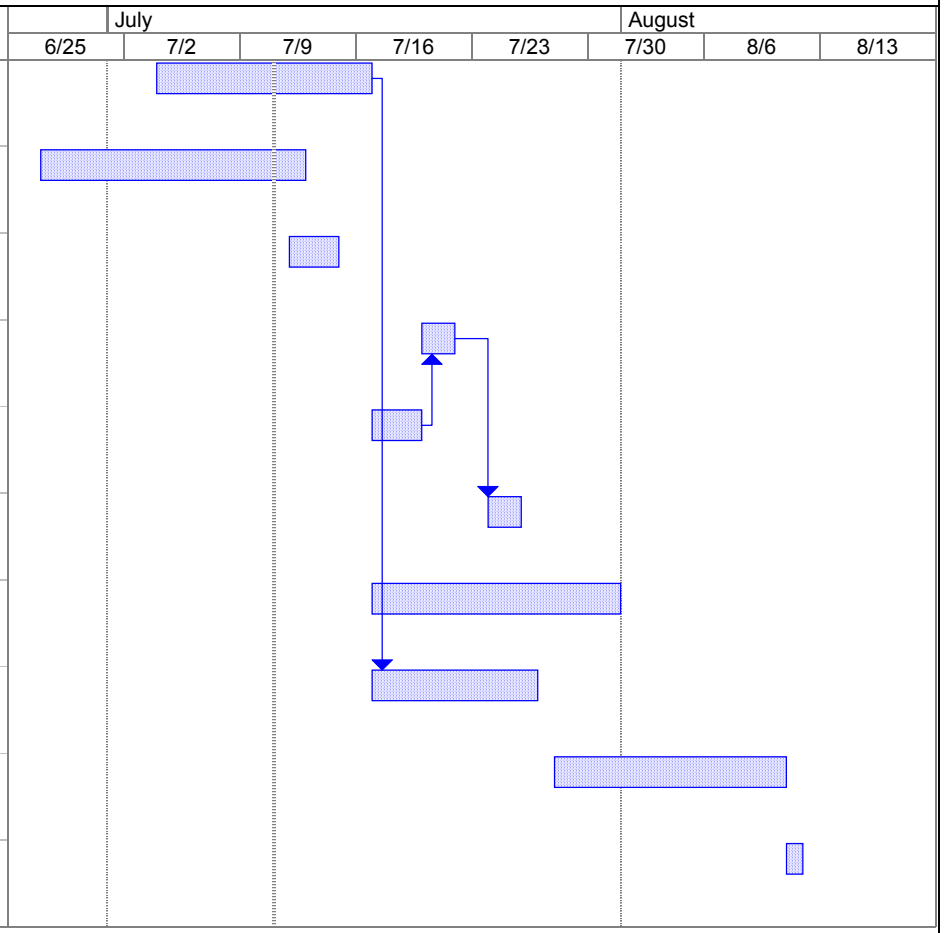
ID	Task Name	Duration	Start	Finish
1	Lime treatment	10 days	Tue 7/4/06	Sun 7/16/06
2	Chip 4" off G-line piers	12 days	Tue 6/27/06	Wed 7/12/06
3	Drill & epoxy dowels @ G-line piers, 10" wall	3 days	Wed 7/12/06	Fri 7/14/06
4	Scaffolding @ G-line	2 days	Thu 7/20/06	Fri 7/21/06
5	Rebar 10" wall @ G-line	3 days	Mon 7/17/06	Wed 7/19/06
6	Shotcrete 10" wall @ G-line	2 days	Mon 7/24/06	Tue 7/25/06
7	Mat pour #1 bottom rebar	11 days	Mon 7/17/06	Mon 7/31/06
8	Utilities under mat	8 days	Mon 7/17/06	Wed 7/26/06
9	Mat pour #1 top mat rebar	10 days	Fri 7/28/06	Thu 8/10/06
10	Place mat slab pour # 1	1 day	Fri 8/11/06	Fri 8/11/06
